



APC Guidance Note **Procurement and Tendering**

By Roshan de Silva,
BSc(Hons)QS, LL.M (Construction Law), MRICS, MAIQS, CQS

APCCoaching.me

1. Introduction

1.1 Purpose of this guidance note.

This guidance note explains, in practical yet technically sound language, how procurement and tendering decisions influence cost, value, risk, and project outcomes throughout the life of a construction project. It serves both as a professional guidance reference and an APC preparation manual for RICS and AIQS candidates pursuing the Quantity Surveying and Construction pathway.

The material aligns with the RICS Procurement and Tendering Guidance Note (2nd Edition), NRM 1, FIDIC 1999/2017, and the AIQS Cost Management Manual, ensuring that readers can relate theoretical frameworks to real-world applications. It enables candidates to connect the principles of commercial management, procurement strategy, and tender evaluation with the competencies assessed at APC Levels 1, 2, and 3, supporting both technical mastery and professional judgment.

1.2 Why Procurement and Tendering Matters

Procurement and tendering are fundamental to achieving value for money and commercial integrity in construction. The chosen procurement strategy defines the contractual relationships, allocation of risk, and control over time, cost, and quality, determining the project's success long before work begins on site.

Moreover, Procurement defines who does what, when, and under what risk profile. A wrong procurement choice can undermine cost certainty, delay delivery, or cause contractual disputes. Conversely, a well-designed procurement strategy aligns every party's commercial incentive with the client's objectives.

Sound procurement ensures that each party understands its responsibilities, that competition is fair and transparent, and that design intent aligns with budget expectations. A robust tendering process builds market confidence, secures qualified contractors, and protects the client from cost escalation or contractual disputes.

From an APC perspective, this topic demonstrates the Quantity Surveyor's role as a strategic commercial advisor, not merely a cost estimator. Candidates who can explain how procurement shapes project outcomes and justify their recommendations using risk, time, and market reasoning exhibit the highest level of professional competence expected at Level 3.

2. Understanding the Competency

2.1 Definition and Overview

Procurement and Tendering is one of the most critical competencies in the RICS Quantity Surveying & Construction Pathway and is equally vital under the AIQS framework. It bridges the gap between design economics and contract administration, testing whether a candidate can identify, justify, and implement the most appropriate route for acquiring construction works or consultancy services.

RICS definition: *"This competency covers how a project is structured and delivered in terms of risk allocation and contractual relationships, and how tendering processes are used to establish a contract price. Candidates should have a clear understanding of the different types of procurement and tendering commonly used, as well as the advantages and disadvantages of each for the parties involved. They should have a detailed working knowledge of the procurement routes and tendering procedures used on their projects".*

AIQS definition: *"Contract Documentation and Procurement involve the various processes by which a construction contract is achieved, including the use of the appropriate project delivery system and standard form of contract, the method of tendering/contractor selection, the provision of bills of quantities, and the subsequent acceptance of a tender.".*

2.2 Competency Levels – RICS / AIQS Expectations

Level	Description
Level 1 – Knowledge	Explain the various procurement routes and tendering methods, including advantages, disadvantages, and risk allocation.
Level 2 – Application	Apply procurement procedures, assist in preparing tender documentation, and participate in evaluations.
Level 3 – Advice	Provide strategic advice on procurement selection, considering time, cost, quality, risk, and market factors.

APC Tip: *When giving Level 3 answers, use the formula "I advised ... because ..." and explain how your advice influenced the client's decision.*

2.3 Procurement vs Tendering

Candidates often conflate these terms. In professional practice and certainly in APC assessment, they must be clearly distinguished.

	Procurement	Tendering
Scope	End-to-end process of acquiring works, goods, or services—from needs analysis to contract award.	Sub-process focused on obtaining and evaluating competitive offers.
Purpose	Defines strategic framework and contractual relationships.	Establishes price and selects supplier/contractor /Subcontractor.
Output Doc.	Procurement Strategy Report, identifying preferred route and rationale.	Tender Evaluation Report and Recommendation for Award.
Timing	Begins during early design/feasibility stages.	Occurs after the procurement route is decided.

Key Message:

Procurement = strategy, Tendering = execution.

Reflection: In practice, the QS must understand both the commercial logic behind procurement and the procedural integrity of tendering. Neglecting either leads to cost and contractual inefficiency.

3. Importance of Procurement in Construction


3.1 Achieving Client Objectives

- Time: Need for early completion or phased delivery.
- Cost: Requirement for budget certainty.
- Quality: Aspiration for bespoke design or performance standards.
- Risk: Appetite to transfer or retain risk.
- Flexibility: Ability to adapt scope during construction.

A procurement strategy translates these into contractual mechanisms.

3.2 Balancing the Project Triangle

Every route sits somewhere on the *time–cost–quality* triangle. For example, Traditional procurement provides cost and quality certainty but limited time flexibility, whereas Management Contracting prioritises programme speed over cost certainty.

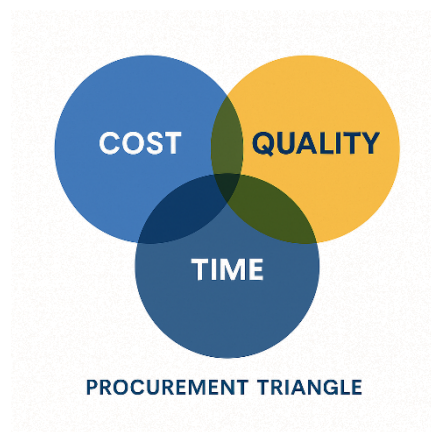

3.3 Impact on Project Success

Evidence from RICS and BCIS studies shows that early procurement planning reduces post-contract variation costs by up to 20 %. Transparent risk allocation and realistic timeframes lead to fewer disputes and more predictable cash flow.

3.4 Client Drivers Influencing Procurement

1. Nature and complexity of the project.
2. Certainty of design and scope.
3. Market conditions and contractor availability.
4. Funding arrangements.
5. Legal and statutory constraints.
6. Sustainability and ICV requirements in the Middle East.

Example: A public hospital project in Oman adopted Design & Build because the Ministry required a fixed completion date to align with equipment procurement. Although design control was reduced, single-point responsibility ensured timely delivery.

Reflection: Procurement is not an academic exercise – it's a strategic business decision defining how risk, money, and responsibility flow through a project.

4. Procurement Framework and Classification

4.1 Overview

A procurement framework is the structured classification of routes available to a client for achieving project delivery. It helps compare alternatives and justify selection based on measurable criteria (time, cost, quality, risk transfer, complexity, control, and flexibility).

4.2 Main Classifications

Category	Key Features	Best Used For
Traditional	Design by Consultant; construction by Contractor; Client retains design risk.	When the design is complete, budget certainty is paramount.
Design & Build	Single entity responsible for design and construction; fast programme.	Where time is critical and design can be defined by a performance spec.
Management Oriented	Contractor manages trade packages on behalf of the client; early start possible.	Large complex projects require overlapping design and construction.
Integrated/ Partnering	Shared risk and reward; long-term collaboration.	Public infrastructure or multi-phase programmes.
Framework/ Serial/Term	Long-term service contracts for repeat work or maintenance.	Clients with continuous programme of similar projects.

4.3 Comparative Analysis of Procurement Routes

Criteria	TR	D&B	MC	CM
Design Responsibility	Client/ Consultants	Contractor	Client	Client
Cost Certainty at Award	High	Medium-High	Medium	Low
Programme Speed	Slowest	Faster	Fast	Fastest
Client Control of Design	High	Medium	High	Very High
Risk to Client	Low	Medium	High	Very High
Suitability for Complex Projects	Moderate	Moderate	High	High

Reflection: No single procurement route is "best." The professional skill lies in matching the route to the project's drivers and the client's risk appetite

5. Working Arrangements in Procurement

Working arrangements describe the contractual and managerial relationships established between the client, designer, and contractor to deliver a project.

Each arrangement affects risk allocation, communication flow, programme sequencing, and payment mechanism

5.1 Traditional Procurement

The client appoints consultants to complete the design, prepares detailed tender documentation (drawings, specifications, BOQ), and invites contractors to price the works on a lump-sum or re-measured basis.

Key Features


- Sequential process: design → tender → construction.
- Employer retains design responsibility.
- Contractor is responsible for execution and workmanship.
- Often governed by FIDIC Red Book 2017 or JCT Standard Building Contract.

Advantages

- High cost and design certainty before award.
- Competitive tendering ensures transparency.
- Clear risk allocation simplifies dispute resolution.

Disadvantages

- Longer pre-construction period.
- Limited contractor input in buildability or value engineering.
- Variations may arise if design errors or omissions exist.

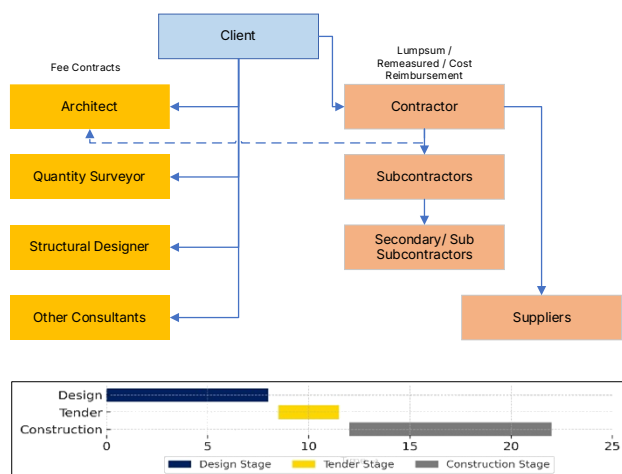

Example: A government hospital project in Muscat used Traditional procurement to guarantee a fixed OMR budget. The design was completed before the tender, and the FIDIC Red Book 1999 was adopted to maintain design control.

APC Tip: At Level 2, demonstrate your understanding of how the preparation of the BOQ and preamble notes align with the risk transfer in a Traditional contract.

5.2 Accelerated Procurement


A variation (modified version) of the traditional approach, where design and construction overlap to reduce programme duration.

Key Characteristics

- Early works packages (e.g., piling, foundations) released before design completion.
- Requires strong change-management controls.
- May adopt a re-measurable contract form to accommodate design development.

Risks & Mitigation

- Design changes during construction → re-measurement claims.
- Supply chain pressure → quality issues or site congestion.
- Mitigate through clear early-works scope and change approval procedures.



Reflection: Time gained through fast-tracking is often offset by disruption and claims if coordination is poor, and the balance between the programme and contractual risk is considered.

5.3 Design & Build (D&B)

A single contractor undertakes both design and construction, providing a single point of responsibility for the client.

Variants


1. Pure D&B: Contractor develops the design from employer's performance requirements.
2. Novated D&B: Consultant design team transferred to contractor post-tender.
3. Turnkey (EPC): Contractor delivers a fully operational facility.

Advantages

- Shorter overall programme.
- Clear accountability and reduced interface risk.
- Cost certainty if scope well defined.

Disadvantages

- Employer has less design control.
- Difficult to assess true value during tender without detailed spec.
- Quality depends on how well performance criteria are written.

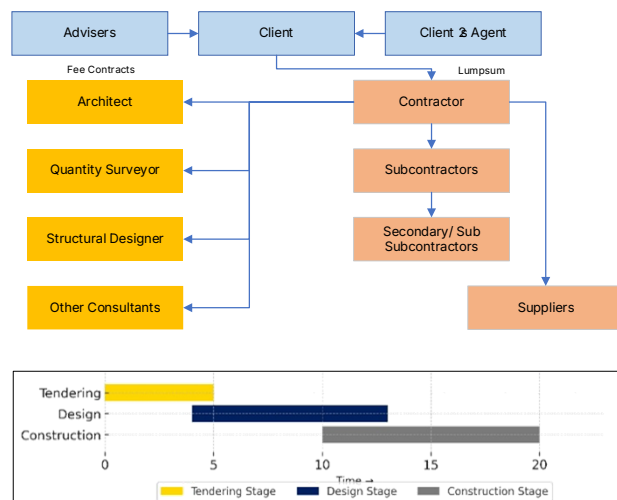

Example: A logistics warehouse in Dugm was delivered under Design & Build using FIDIC Yellow Book 2017. Performance specifications for thermal insulation and floor flatness ensured compliance without over-specifying materials.

APC Tip: At Level 3, explain how you advised on drafting performance requirements to retain quality control while allowing contractor innovation.

5.4 Management Contracting

A Management Contractor is appointed early to manage and coordinate a series of work packages let to Works Contractors. The Management Contractor is paid a fee plus reimbursable costs.

Features



- Early contractor involvement.
- Flexibility to start construction before overall design completion.
- Employer retains ultimate responsibility for trade contracts.

Advantages

- Overlapping design and construction reduces the programme.
- Greater buildability input from the market.
- Transparent cost control through open-book procurement.

Disadvantages

- Cost certainty is achieved only after all packages are procured.
- Complex administration with multiple contracts.
- Employer bears the risk of package failure.

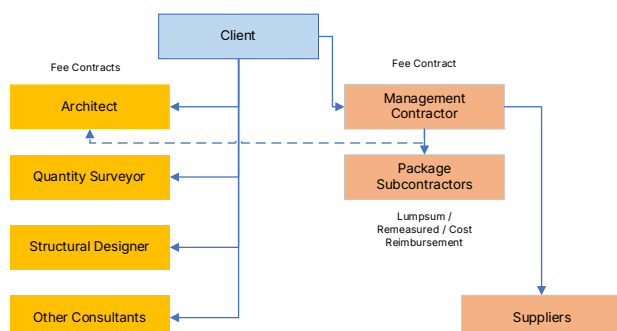


5.5 Construction Management

Definition:

Similar to Management Contracting, but each trade contractor contracts directly with the employer. The Construction Manager acts only as an agent.

Implications

- Maximum client control and visibility.
- No contractual liability of CM for trade contract performance.
- Requires an experienced client and a strong project management team.

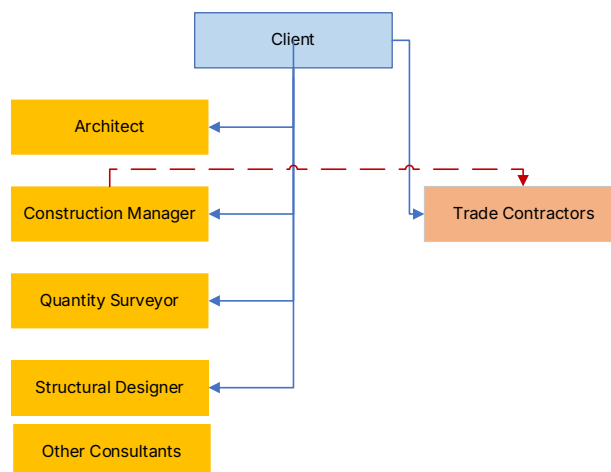

Example: A Riyadh stadium project used Construction Management for overlapping steelwork and façade packages. The client accepted direct risk for interfaces but saved five months on the programme.

Reflection: Use Management or Construction Management when time is the driver and the client is mature enough to manage multiple contracts.

6. Relationship-Based and Finance-Based Procurement

6.1 Partnering and Alliances

Concept:

These arrangements are built on mutual trust, transparency, and shared objectives rather than strict adversarial contracts.

Core Principles

- Shared goals and KPIs (time, cost, quality, safety).
- Open-book cost management.
- Joint risk management and pain/gain share mechanism.
- Continuous improvement through collaboration.

Examples:

- NEC Option C (Target Cost Contract).
- FIDIC Alliance Model (2023 draft).
- Local partnering frameworks for government projects.

*Reflection: Partnering works best when there is long-term trust and shared commercial incentive, not simply because a contract labels itself 'partnering'.**

6.2 Public-Private Partnership (PPP) / Private Finance Initiative (PFI)

A private consortium designs, builds, finances, and operates a public asset for a concession period (typically 20–30 years) before handing it back to the state.

Key Elements

- SPV (Special Purpose Vehicle): a project company formed by investors.
- Funding structure: mix of debt and equity.
- Payment mechanism: availability or usage-based.
- Risk transfer: design, construction, and operation risks transferred to SPV.

Example: A wastewater treatment plant in the UAE was delivered via PPP. The consortium financed construction and operated the plant for 25 years under a build-own-operate-transfer (BOOT) model.


APC Tip: At Level 1, explain PPP in terms of risk transfer and whole-life cost; at Level 3, demonstrate advising on value-for-money and bankability analysis.

6.3 Design & Manage

A hybrid approach where a single entity undertakes design and manages subcontractors but does not directly construct. It combines Design & Build and Management principles.

When to Use

- Complex fit-out or refurbishment works.
- Need for single design control with flexible execution.
- Client prefers to procure trade packages separately.



6.4 EPC / Turnkey

Predominantly used for industrial and energy projects. The contractor delivers a fully functional facility ready for operation at a fixed price and date.

Characteristics

- Maximum risk transfer to the contractor.
- Performance guarantees and liquidated damages are common.
- Typical form: FIDIC Silver Book 2017.

Reflection: In EPC projects, the QS must be alert to hidden risk premiums embedded in the price. "Risk transfer" is never free.

7. Other Procurement Approaches

7.1 Term Contract

Used for maintenance or minor works over a period rather than for a single project.

Features

- Fixed schedule of rates.
- Measured as and when work is ordered.
- Offers efficiency for repetitive tasks.

7.2 Call-Off Contract

Allows the client to purchase goods or services from an approved supplier list as required, without a new tender each time.

Example: Utility company issuing call-offs for pipe-laying contracts under a framework agreement.

7.3 Serial Contract

Repetition of similar works using rates from a previous competitive tender. This reduces procurement costs for standardised housing or school projects.

7.4 Framework Agreements

Establish a panel of contractors to undertake future works without re-tendering each time. Can be single-supplier or multi-supplier. Often used by public authorities to secure long-term value and quality.

Reflection: Frameworks and serial contracts focus on efficiency and relationship continuity, not on bypassing competition.

8. Contract Types and Forms of Contract

8.1 Role of the Contract Form

The form of contract translates the procurement strategy into legal terms. It defines responsibilities, procedures, and risk sharing. Selecting the wrong form can nullify the benefits of a well-chosen procurement route.

8.2 Common Standard Forms

Form	Typical Use	Core Principle	Strength
FIDIC 1999 / 2017	International construction & infrastructure	Balanced risk allocation with Engineer's role	Widely recognised and adaptable
NEC 4	Collaborative UK projects	Mutual trust and early warning mechanisms	Promotes transparency and risk management
JCT 2016	UK building works	Prescriptive clauses and traditional roles	Familiar to design-led projects
ICChemE / ICE	Process and civil engineering	Detailed technical and design clauses	Ideal for industrial plants
Bespoke Forms	Local authorities or developers	Tailored to local law and policy	Flexibility for unique requirements

Example: An Omani airport project used a modified FIDIC Silver Book to incorporate Oman PDPL clauses and ICV reporting requirements.

8.3 Risk Allocation and Payment Mechanisms

Payment Basis	Description	Common Use
Lump Sum	Fixed price for defined scope	Traditional, D&B
Re-measurable	Paid on actual quantities measured on site	Infrastructure works
Cost-Plus	Actual cost + fee or percentage	Emergency or research projects
Target Cost / Pain-Gain	Incentivised to share savings or overspends	Partnering & Alliance contracts

Reflection: Every payment mechanism balances risk and incentive. Understanding cashflow impact and risk transfer is central to Level 3 competence.

9. Introduction to Tendering

Tendering is the formal process of inviting, receiving, and evaluating offers from suppliers or contractors to undertake construction works or provide services. It ensures value for money, fair competition, and transparency in contract award.

9.1 Objectives of Tendering

- Obtain competitive prices for defined work.
- Identify the most economically advantageous tender.
- Ensure transparency and fairness.
- Provide an audit trail for procurement decisions.
- Support local participation and in-country value.

9.2 Key Principles

1. Equality of Treatment – all bidders receive the same information.
2. Transparency – process must be traceable and defensible.
3. Accountability – decisions must be supported by evidence.
4. Confidentiality – protect commercial information.
5. Value for Money – balance cost, quality, and risk.

Reflection: Tendering is not just about finding the lowest price – it's about identifying the offer that delivers best value and minimal risk to the client.

10. Tendering Strategies

Different tendering strategies suit different procurement routes and market conditions.

Strategy	Description	Advantages	Disadvantages
Open	Any qualified contractor can submit a bid.	Encourages competition and transparency.	High admin cost; may attract unqualified bidders.
Single Stage Selective	Only prequalified contractors are invited.	Ensures competence and capacity.	Reduces competition.
Two-Stage Selective	Stage 1: preliminary tender; Stage 2: negotiated fixed price.	Early contractor input; better buildability.	Cost certainty only after Stage 2.
Negotiated	Direct negotiation with one contractor.	Speed and confidentiality.	Lack of open competition.
Framework / Call-Off Tendering	Pre-agreed rates applied to specific work packages.	Saves time for repeat work.	May reduce price tension.
E-Tendering	Digital submission and evaluation.	Efficiency, auditability, and transparency	Requires a robust system and cybersecurity

Example: An Omani infrastructure project adopted a two-stage selective tender. Early contractor input during Stage 1 allowed value engineering that reduced piling cost by 12 % before fixing the final lump sum.

APC Tip: At Level 3, explain the reason for selecting a method – e.g., "Two-stage was recommended to allow early market engagement where design was 60 % complete."

11. Prequalification of Bidders

Prequalification (PQ) ensures only capable and financially sound contractors are invited to tender.

11.1 Purpose

- Reduce risk of non-performance.
- Save evaluation time by filtering unqualified firms.
- Encourage fair competition among competent bidders.

11.2 Common PQ Criteria

1. Financial stability (audited accounts, cash flow).
2. Technical capability and experience.
3. Resources and key staff CVs.
4. Quality, safety, and environmental systems.
5. Legal standing and certifications.
6. Local partnership or ICV compliance.

11.3 Evaluation of PQ Submissions

Use a weighted matrix, e.g.:

Criteria	Weight	Bidder A	Bidder B	Bidder C
Financial Strength	25 %	23	25	18
Technical Experience	35 %	32	30	33
Resources & Staff	15 %	14	12	13
HSE & QA/QC	10 %	9	9	10
Local Participation	15 %	13	12	15
Total	100 %	91	88	89

Reflection: *Always record reasons for inclusion/exclusion – procurement audits and APC assessors both focus on procedural integrity.*

12. Invitation to Tender and Documentation

The Invitation to Tender (ITT) is the formal package issued to prequalified contractors. It sets out the scope, terms, and submission requirements.

12.1 Typical ITT Contents

- Letter of Invitation
- Instructions to Tenderers
- Form of Tender
- Conditions of Contract
- Specifications and Drawings

- Bill of Quantities or Schedule of Rates
- Programme requirements
- Tender Bond / Performance Bond format
- Addenda acknowledgement forms

12.2 QS Role

The QS prepares tender documentation, checks consistency between drawings, specifications, and BOQ, and coordinates clarifications during the tender period.

Example: *In a mixed-use development, the QS issued ITT via an e-tendering platform (Aconex). Clarifications were managed through controlled threads, ensuring traceability for audit and post-tender analysis.*

APC Tip: *Discuss how you ensured consistency across documents and responded to bidder clarifications – this demonstrates Level 2 competence.*

13. Tender Queries, Site Visits, and Addenda

13.1 Clarifications and Queries

Tenderers may submit questions seeking clarification on design or scope. Responses must be distributed simultaneously to all bidders to maintain fairness.

Best Practice

- Maintain a clarification register.
- Number each query and response.
- Issue clarifications via official addenda only.
- Avoid direct communication outside the tender portal.

13.2 Site Visits

Provide bidders with equal opportunity to inspect site conditions. Record attendance and distribute minutes of the visit.

13.3 Addenda

Issued to modify or clarify tender documents before submission. Each addendum should state:

- Addendum number and date.

- Sections or drawings affected.
- Clarification or replacement text.

Reflection: *Addenda control ensures the principle of equality of information, a fundamental RICS ethical standard.*

14. Tender Submission, Opening, and Evaluation

14.1 Submission

- Bidders must submit tenders before the deadline in the specified format.
- Submissions may be electronic or hard copy under seal.
- Late tenders are typically rejected to preserve fairness.

14.2 Opening

- Conducted by authorised personnel in the presence of a witness (for public tenders).
- Record all received bids, time stamps, and signatures.

14.3 Evaluation Process

A structured evaluation compares tenders for compliance, quality, and price.

Stages

1. Preliminary Check: completeness, signatures, bonds, addenda acknowledgments.
2. Technical Evaluation: methodology, programme, resources, HSE, QA/QC.
3. Commercial Evaluation: arithmetical check, pricing analysis, exclusions.
4. Normalisation: adjust for discrepancies or missing items.
5. Clarifications: seek written confirmation for ambiguous rates or exclusions.
6. Recommendation: Identify the lowest *compliant* tender or best-value offer.

14.4 Reporting

The QS prepares a Tender Evaluation Report summarising:

- Methodology used.
- Comparison tables (technical and commercial).
- Adjustments and normalisation.
- Recommendations with justification.

Example: *In a design-build hotel tender, Bidder B initially appeared lowest. After correcting arithmetic and adding excluded scope, Bidder C became most competitive – reinforcing the importance of a transparent normalisation process.*

APC Tip: *In the interview, expect to be asked how you ensured fairness and integrity during evaluation – mention traceability and documented reasoning.*

15. In-Country Value (ICV) and Localisation Policies

In the Gulf region, many government entities adopt ICV frameworks to maximise local economic participation.

15.1 Objectives

- Encourage employment of nationals.
- Promote local manufacturing and services.
- Support SME (Small & Medium Enterprise) development.
- Retain economic value within the country.

15.2 Evaluation Integration

ICV often forms a weighted component in tender evaluation (5–20 % of total score). Bidders must submit ICV certificates or plans showing:

- Percentage of Local (National) content.
- Local staff ratio.
- Subcontracting to SMEs.
- Training and capacity-building initiatives.

Reflection: The QS plays a critical role in verifying ICV compliance and ensuring that cost evaluations remain transparent while supporting national policy objectives.

16. Contract Award and Governance

16.1 Recommendation for Award

After evaluation, the QS prepares a formal recommendation to the client including:

- Summary of process followed.
- Final evaluation results.
- Justification for the recommended bidder.
- Confirmation of compliance with procedures.
- Draft Letter of Acceptance or Letter of Intent.

16.2 Post-Tender Negotiations

May be conducted to clarify minor issues or finalise terms, but must not alter competitive fairness.

16.3 Contract Formation

Occurs when:

- Letter of Acceptance issued and acknowledged, or
- Contract agreement signed by both parties.

16.4 Governance and Audit

Maintain a complete audit trail:

- Tender invitation and correspondence.
- Evaluation sheets and minutes.
- Approvals and award letters.

APC Tip: Emphasise that professional ethics require objectivity and documentation – “If it isn’t documented, it didn’t happen.”

17. APC Guidance, Common Pitfalls, and Reflection

17.1 Level 1 – Knowledge

- Define procurement routes and tendering methods.
- Explain the difference between open and selective tendering.
- Discuss how risk allocation influences procurement choice.

17.2 Level 2 – Application

- Describe your role in preparing ITT, responding to queries, or evaluating bids.
- Show involvement in PQ assessments and tender reports.

17.3 Level 3 – Advice

- Demonstrate reasoned advice on route and method selection.
- Explain how your advice influenced client decision-making.
- Discuss lessons learned and improvements to process.

Q: How would you advise a client selecting between Traditional and Design & Build procurement?

A: I would first assess their priorities – if cost and design quality are key, I’d recommend Traditional; if time and single responsibility are crucial, Design & Build offers faster delivery. I’d explain risk implications under FIDIC Red vs Yellow Book, and advise aligning contract conditions with the chosen route.

17.4 Common Pitfalls

1. Confusing procurement and tendering.
2. Failing to record clarifications or addenda.
3. Inadequate normalisation of tender prices.
4. Overlooking local regulations or ICV compliance.

5. Poor justification of recommendations.

17.5 Best-Practice Recommendations

- Engage the QS early during design.
- Use structured evaluation matrices.
- Maintain transparency and fairness.
- Keep thorough records for audit and disputes.
- Review lessons learned after contract award.

Reflection: Procurement and tendering embody the QS's role as a guardian of commercial integrity. Mastery of this competency demonstrates not just technical skill but professional ethics and judgment.

18. References & Further Reading

- RICS Guidance Note: *Procurement and Tendering, 2nd Edition (2019)*.
- RICS *New Rules of Measurement (NRM1 & NRM2)*.
- AIQS *Cost Management Manual, 6th Edition*.
- FIDIC *Red, Yellow & Silver Books (1999/2017 Editions)*.
- NEC4 Engineering and Construction Contract (ECC).*
- RIBA *Plan of Work 2020*.
- Oman Tender Law and ICV Guidelines (2023).
- ISO 10845 – *Construction Procurement Standard*.



"You can dream, create, design, and build the most wonderful place in the world. But it requires people to make the dream a reality." – Walt Disney.
